



GC7 PR Desk Review

Our mission is to support community action to prevent HIV infection, meet the challenges of AIDS, and build healthier communities.



Action Taken from the last review of the Oversight Committee

(GC7 Review by OC on Mar Apr 2025)

S No.	Remarks/Recommendations of the Oversight Committee	Action Taken by PR
1	IHAA to provide information regarding the HR structure of PR, SRs and SSRs, their numbers in different States, their roles and salary bands in different components.	The detail of the staff submitted to CCM
2	Manipur SSR selection was delayed due to the ethnic violence and law and order situation	The selection process completed in April 2025
3	State wise breakup of performance indicators to be provided in quarterly progress reports	Quarterly state wise break of performance indicator submit to CCM and NACO
4	Performance in Quarterly progress reports to be submitted in cumulative format (from beginning of GC7 to that present quarter) as well as in quarter wise format, to the Oversight Committee.	Reports submitted to CCM as recommended
5	Budget Reprogramming approvals and revised plans to be shared with NACO and OC As and when done	Reprograming budget shared with CCM

SR Selection/ On boarding Status

SR Name	State	On boarded (Yes/ No)
Gujarat State Network of People Living with HIV (GSNP+)	Care and Support –Madhya Pradesh and Gujarat and DD&DH Prison Intervention-Gujarat and DD&DH	Yes
Network of Maharashtra positive people (NMP+)	Care and Support – Maharashtra	Yes
Lepra Society	Prison Intervention-Madhya Pradesh	Yes
Udaan Trust	Prison Intervention-Maharashtra	Yes
The Humsafar Trust	Virtual Intervention	Yes

Geographical Coverage SAMAGRA Programme - GFATM



Care & Support Services to PLHIV through 75 CSC Linked with 194 ARTCs.

- Community Lead Outreach Service
- Tracking of Lost to Follow-up Client
- Index Testing
- EVTHS Follow-up
- Viral Load

Coverage: 95-95-99



HIV Coverage in 274 Prison & 534 OCS Centers in 198 dist of 11 state & UT's

- HIV and TB screening
- Behavior Change Communication (BCC) on HIV
- Index Testing
- Linking with Social Protection

Coverage: 95-95-



HIV Coverage to hard to reach population through virtual platforms:

- HIV Testing
- Linkages with the Care
- Behavior Change Communication (BCC)
- Index Testing
- Linking with the other facilities.


Coverage: 95-95-



Strengthening community networks to support countries target on elimination of HIV.

- Strengthening State Level Key Population Network
- Creating Community Feedback Mechanism
- Strengthening Districts Community Resource Group


Beyond: 95-95-99



Budget Utilization of Samagra Project for the period from Apr 2024 to Mar 2026

S. N.	Component	Total Budget (April 2024 to March 2026)	Total Expenditure (April 2024 to March 2026)	Utilization in %	Reason of Variance
1	Care Support Center 2.0	8,858,374	7,687,922	87%	The initiation of key interventions, including 120 Paperless ART sites, Mental Health services, and Index Testing, will contribute in increasing the utilization in the coming months.
2	CSS	498,903	55,779	11%	CSS activities budgeted in this period. the activities has been now executed at the field as per the NACO approval and guidance
3	Prison	1,190,561	785,453	66%	The Handheld X-ray initiative is progressing at full pace and is expected to increased the utilization.
4	RRB	5,403	5,352	99%	
5	Virtual intervention	601,037	547,270	91%	
Total		11,154,279	9,081,776	81%	


GC7 Key Performance Indicator 1- Percentage of people living with HIV and on ART with viral load test result

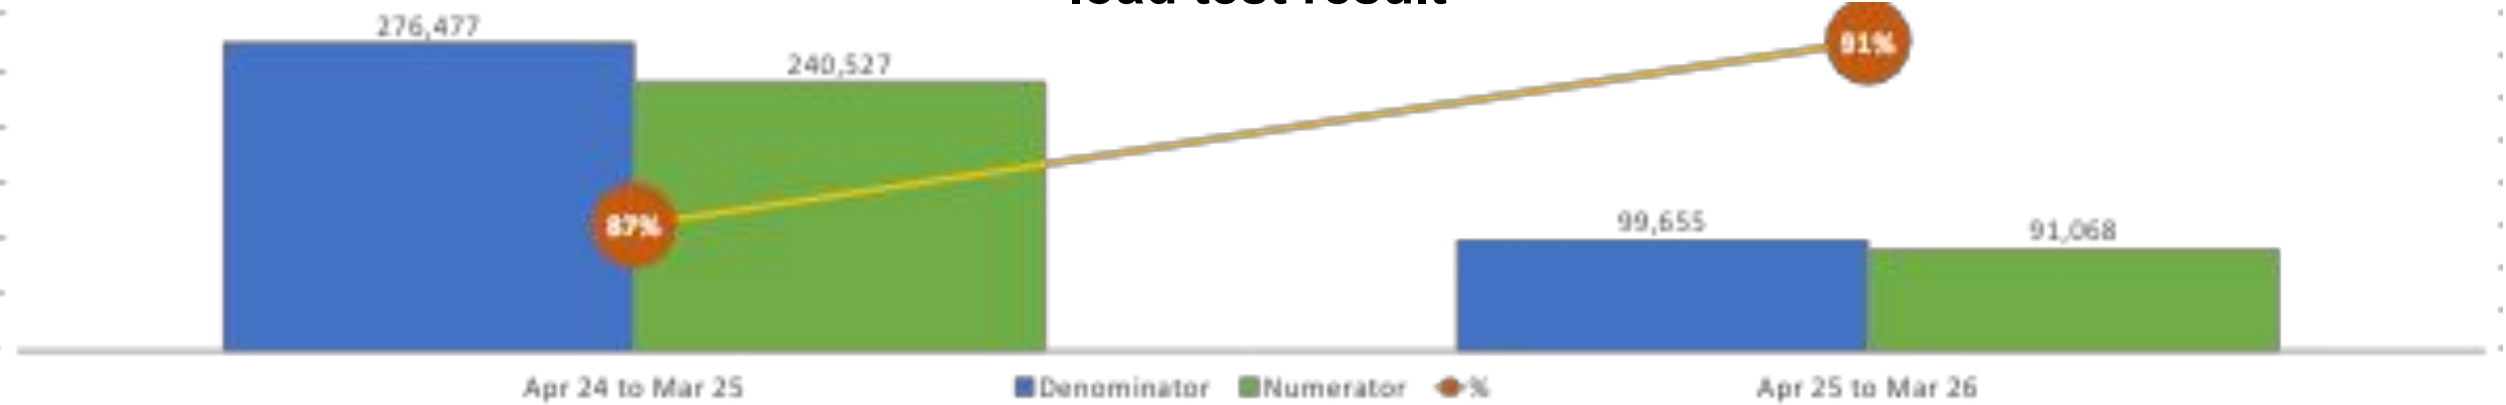

Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	2,40,527	91,068	3,31,595	April to Sept, 24 all due cases was shared for VL testing, however from October 2024 onwards only overdue cases were considered as target. Around 4% of the people tested for VL in subsequent reporting cycle in Y2 A significant number of people reported as dead or opted out from the programme	CSC 2.0 MPR
Denominator (Target)	2,76,477	99,655	3,76,132		
Achievement %	87%	91.38%	88.16%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Active follow up for mobilisation of PLHIV who need to undergo for testing	On going
2	Treatment literacy for PLHIV and importance of VL testing imparted during SGM, FGD and peer counselling	On going
3	Sample collection was done where client could not able to reach to ARTC such as prison, elderly and bed ridden clients	On going
4	Emergency travel support	On going


GC7 Key Performance Indicator 2- Percentage of PLHIV on ART who are Lost to follow up (LFU) tracked with definite outcome



Key Performance Indicator	Y 1 Achievement	Y 2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	1,26,659	50,540	1,77,199	In the first PU (Apr'24 to Sep'24) MIS+LFU was consider in the target and its achievement. From October 2024 onwards only LFU cases and it outcomes considered in the numerator and denominator.	CSC 2.0 MPR
Denominator (Target)	1,59,306	64,010	2,23,316		
Achievement %	79%	79%	79%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Address verification drive to update the contact detail of all PLHIV who are on active care	On going
2	Collecting of alternative address of LFU untraceable	On going
3	Tracking of LFU cases on Regular basis and conducting drive twice in the year	On going
4	Data Triangulation within ARTC of 13 states with aim to identify the duplicate cases who are taking ART from one ARTC and show LFU in another ARTC	Completed


GC7 Key Performance Indicator 3- Percentage of other vulnerable populations that have received an HIV test during the reporting period and know their results (Index testing)



Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	11,614	8,617	20231	The cases are being followed and tested in subsequent quarters	CSC 2.0 MPR
Denominator (Target)	12,440	8,748	21,188		
Achievement %	93.36%	98.50%	95.48%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Index testing campaign initiated for identification of eligible index partner	On going
2	CBS has rolled out in MP and Mizoram, and requested Gujarat, Maharashtra and Manipur SACS to start CBS for index partner testing	On Going


GC7 Key Performance Indicator 4- Percentage of HIV-exposed infants tested for HIV at 6 months of birth.

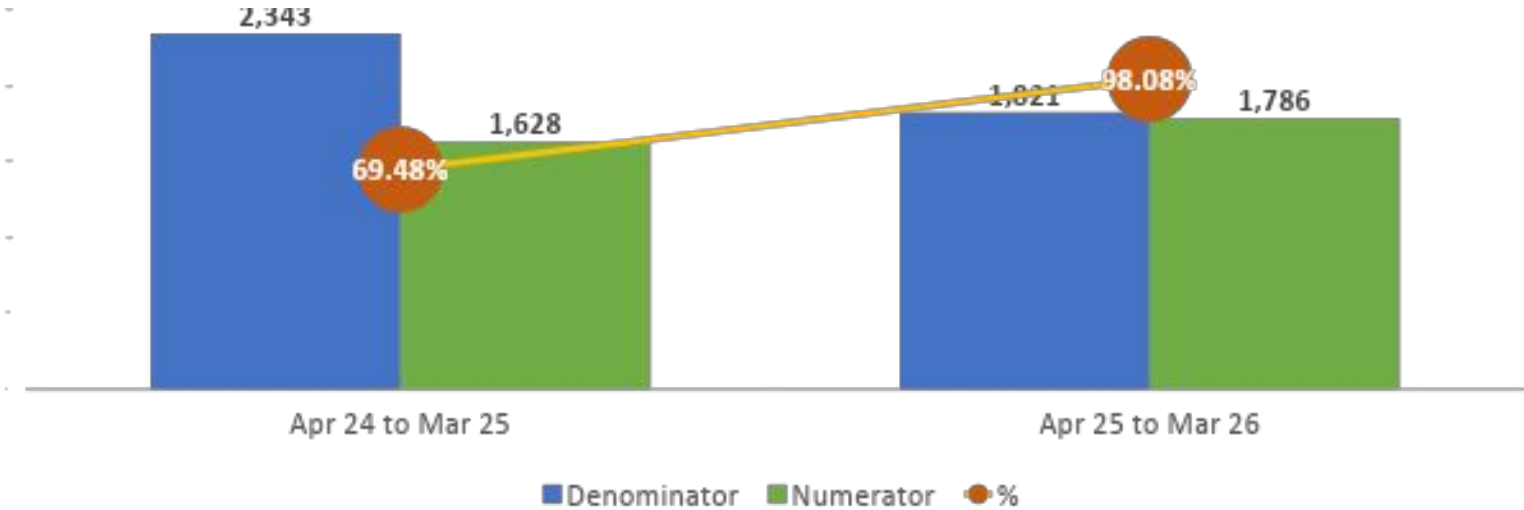

Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	1,628	1,786	3,414	In the first PU (Apr'24 to Sep'24) we have reported the number shared by Plan and SAATHII.	CSC 2.0 MPR
Denominator (Target)	2,343	1,821	4,164		
Achievement %	69.48%	98.08%	81.99%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Proactive follow up for HEI for EID testing and continued till final EID is done	On going
2	Some PPW migrated to their maternal home, though active follow up, testing is been conducting in their native place	On going


GC7 Key Performance Indicator 5- Number of people in prisons and other closed settings that have received an HIV test during the reporting period and know their results.



Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	3,48,936	4,34,017	7,82,953	The yearly target of prison was consider as semester target, which was rectified in year 2, the overall performance of Prison HIV coverage in more the 100%	Prison MPR
Denominator (Target)	3,19,591	3,78,920	6,98,511		
Achievement %	109.18%	114.54%	112.09%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Peer prison volunteer identified and trained on HIV service cascade	On going
2	HIV screening is done in prison and other closed setting	On going
3	BCC and Stigma related camps were organised inside the prison to sensitise inmates	On going


GC7 Key Performance Indicator 1- Percentage of ICTC-ARTC Linkage Loss brought back with definite outcomes

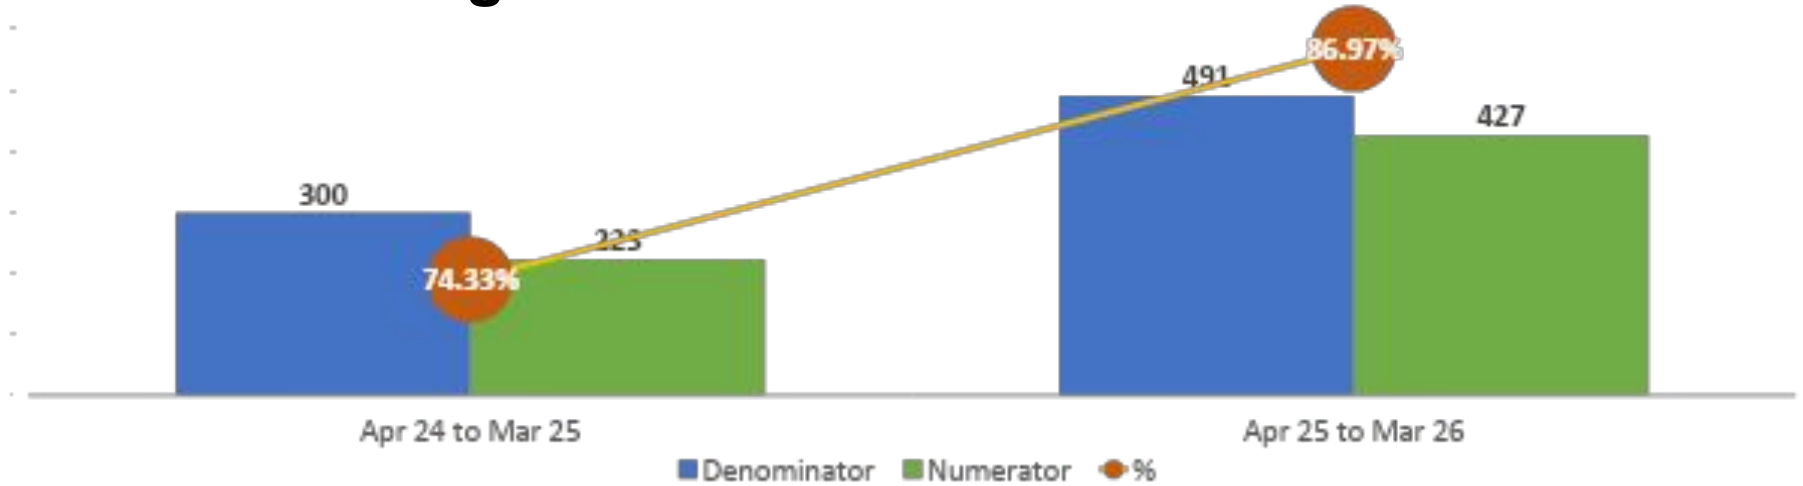

Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	223	427	650	Untraceable, migrated old cases shared by some ICTC and target is counted every six month in our line list.	CSC 2.0 MPR
Denominator (Target)	300	491	791		
Achievement %	74.33%	86.97%	82.17%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Treatment preparedness counselling is provided to PLHIV and link them with ARTC	On going
2	Index testing for their family member/sexual partner is conducted	On going


GC7 Key Performance Indicator 5- TB notification among Prison Inmates



Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	262	298	560	The TB case identification is low through verbal screening, to address low case finding hand held Xray initiative is launched in January 2026	Prison MPR
Denominator (Target)	300	350	650		
Achievement %	87%	85%	86.2%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	TB screening of all inmate is carried out with active case finding	On going
2	TB positive cases linked with ATT	On going


GC7 Key Performance Indicator 2-Percentage of PLHIV newly initiated on ART followed up



Key Performance Indicator	Y1 Achievement	Y 2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	25,480	24,824	50,304	There are more than 6% Death cases among newly initiated cases and 3% opt out from the programme including taking treatment from private provider and 1% cases stopped treatment or transferred out.	CSC 2.0 MPR
Denominator (Target)	28,499	28,011	56,510		
Achievement %	89.41%	88.62%	89.02%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Six month adherence support provided to PLHIV and active follow up, addressing stigma, linking with social protection and entitlement	On going
2	Index testing for newly initiated are conducted	On going


GC7 Key Performance Indicator 3- Percentage of PLHIV on-ART MIS brought back with definite outcomes



Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	87,345	-	87,345	This line list has been discontinued by the NACO.	CSC 2.0
Denominator (Target)	1,18,469	-	1,18,469		
Achievement %	73.74%	-	73.74%		


S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	This activities has been discontinued by the NACO	

GC7 Key Performance Indicator 5- Percentage of newly diagnosed /known HIV Positive Pregnant Women (PPW) & PPWs tested for VL test between 32-36 weeks



Key Performance Indicator		Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)		1183	2011	3194	During the first PU period (Apr'24 to Sep'24), we did not receive data from ARTC. The legacy data from the other PRs (PLAN and SAATHII) was received only in August 2024. NACO sent communication to include EVTHS in CSC on 30 th Sept 2024 and from Oct onwards the data sharing process started Data sharing from the ART center started after the communication, as a result performance was affected during Y1.	CSC 2.0 MPR
Denominator (Target)		2052	2028	4080		
Achievement %		57.65%	99.16%	78.28		
S No.	Activities which were planned to be conducted with respect to this KPI					Status
1	Proactive follow up for PPW for VL testing, and encouraging institutional delivery					On going
2	Follow up for WLHIV for post natal cases					On going


GC7 Key Performance Indicator 6- Percentage of HIV-exposed infants tested for HIV at 6 weeks, 6 months, 12 months and 18 months of birth or 3 months after cessation of breastfeeding, whichever is later.



Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	5064	7613	12,677	In the first PU we have reported the achievement done by the PLAN/SAATHII and work on the data shared by them. NACO sent communication to include EVTHS in CSC on 30 th Sept 2024 and from Oct onwards the data sharing process started The performance has improved from October 2024 onwards	CSC 2.0 MPR
Denominator (Target)	6452	8078	14,530		
Achievement %	78%	94%	87.25%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Proactive follow up for HEI for EID testing and continue in case till final EID is done	On going
2	Some PPW are migrated to their maternal home, though an active follow up, testing is been conducting in their native place	On going


GC7 Key Performance Indicator 7- Percentage of PLHIV on 3rd line ART followed up



Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	442	1,130	1,572	N/A	MPR
Denominator (Target)	442	1,136	1,578		
Achievement %	100%	99.47%	99.62%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	The six month adherence support is provided to PLHIV who have initiated for 3 rd line ART	On going
2	The client's index is tested for HIV and service cascade concluded with VL testing	On going


GC7 Key Performance Indicator 8- Percentage of PLHIV with unsuppressed Viral Load followed up

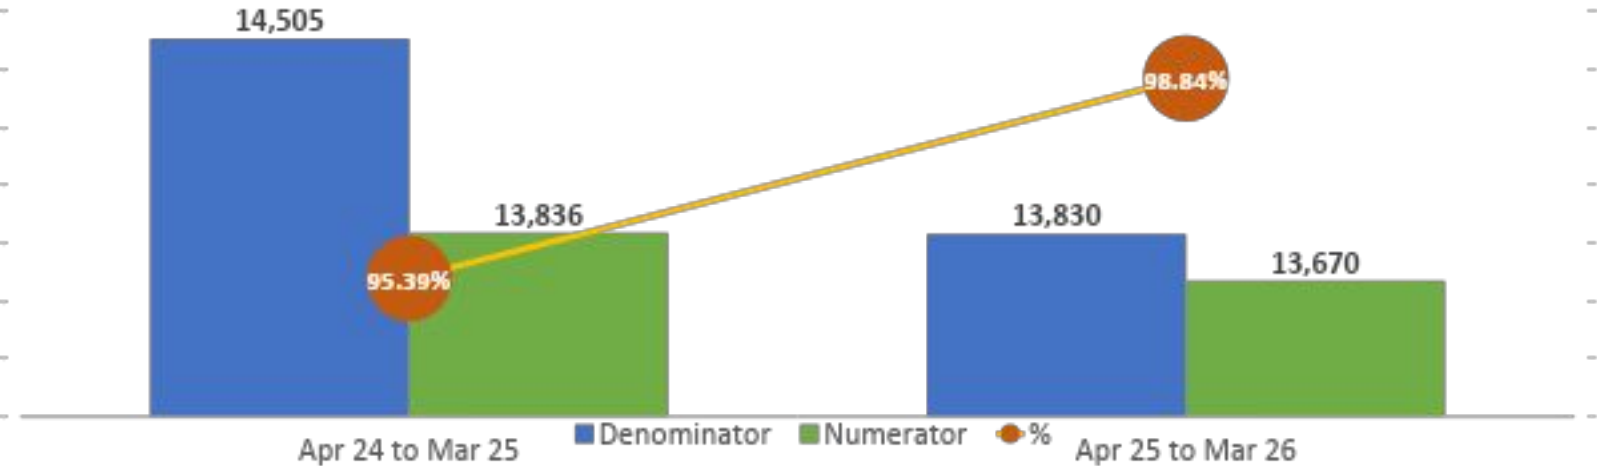

Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	13,836	13,670	27,506	In the first PU unsuppressed line list not shared. Numerator is VL testing after EAC	CSC 2.0 MPR
Denominator (Target)	14,505	13,830	28,335		
Achievement %	95.38%	98.84%	97.07%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	The six month adherence support is provided to PLHIV who have unsuppressed VL count, additional support for EAC provided	On going
2	The client’s partners tested for HIV and service cascade concluded with repeat VL testing	On going

GC7 Key Performance Indicator 9- Percentage of PLHIV with TB followed up for ART and ATT

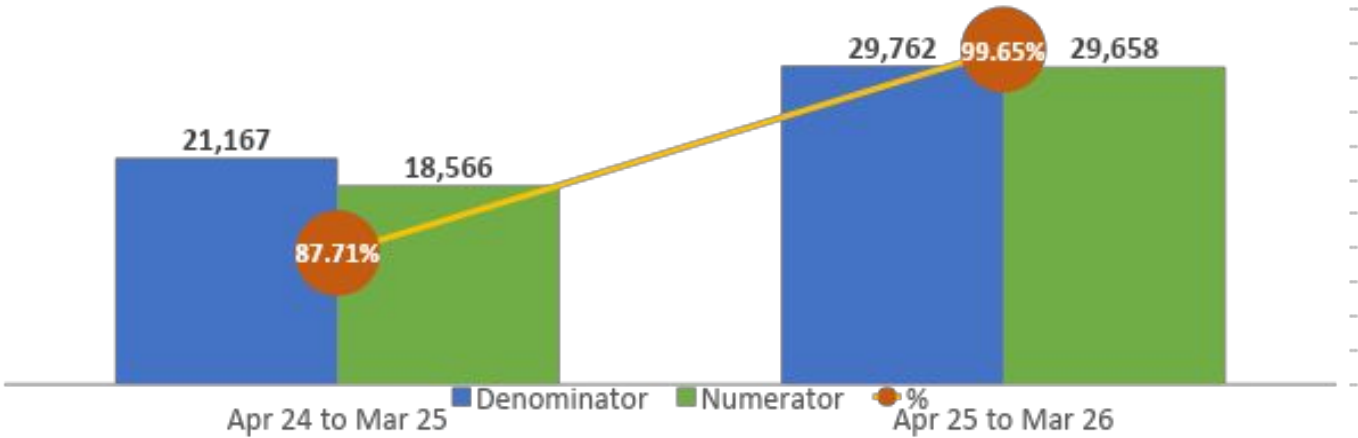

Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	18,566	29,658	48,224	The adherence support is provided to PLHIV on ATT	
Denominator (Target)	21,167	29,762	50,929		
Achievement %	87.71%	99.65%	94.68%		


S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Adherence support provided till the ATT is completed	On going
2	The client’s partners tested for HIV	On going
3	Family members are screened for TB and if found positive, ATT initiated	On going

GC7 Key Performance Indicator 10- Percentage of PLHIV with Comorbidities (other than TB)-Unstable on ART/uncontrolled comorbidities followed up

Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	347	0	347	This activities has not started	Data started sharing only in Oct'24 CSC MPR
Denominator (Target)	347	0	347		
Achievement %	100.00%	0	100.00%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	The activities has not started	Not stated
2	CSC is carrying the awareness on Cervical cancer, mental health etc.	On-going

GC7 Key Performance Indicator 1- Percentage of HIV positive Inmates on ART during the reporting period



Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	682	961	1643	The missed cases in each reporting period is subsequently linked with ART in next reporting cycle	MPR
Denominator (Target)	717	982	1699		
Achievement %	95%	97.9%	96.7		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Address verification of the newly diagnosed inmate are being done with the support of CSC, adherence support is being provided by the Prison Coordinator	On going
02	Plan for post release linkage with inmate and linked to ART once is released from the prison	On going

GC7 Key Performance Indicator 1- Number of State CRG meeting conducted

Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	11	9	20	- In Year 2, 9 states conducted SCRG meetings (DNH & Goa Pending) - CSS activities were put on hold during April to Sept 2025	Letter from respective SACS for SCRG formation
Denominator (Target)	11	11	22		
Achievement %	100%	81%	90.9 %		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	The support to State CRG continue provided	On Going

GC7 Key Performance Indicator 2- Number of District CRG committee formed

Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	112	23	135	In year -1 communication was to form DCRG in high priority dist. (47). But later the number of DCRG was revised by NACO There are 61 DCRG remaining in the 9 states J&K-22, UK-9,Gujarat-3,MP-6, MH -9, DNH-2,Goa -2,Ladakh -2, Manipur -8	Letter from SACS to all DACO or DTO
Denominator (Target)	47	149	196		
Achievement %	238%	15	67%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
01	The efforts to established 61 D-CRG are going on with national, state KP network, TI and PLHIV network	Going on
02	Coordination with SACS to push the D-CRG formation	Going on

GC7 Key Performance Indicator 3- Number of Community Champions trained on CLM

Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	0	291	291	Y1 – CLM guidelines being developed. Induction training conducted for 70 CC in Manipur, 50 CC in Mizoram based on the drop out of CCs The communication on training as well as with guidance came in January 2026 from NACO CLM training - 291 CCs trained since January 2026 through 14 batches (Gujarat- 5 batches, MP- 5 Batches, UK-1, Jammu- 1, MHA- 2) up to March 2026	
Denominator (Target)	1686	1002	2688		
Achievement %	0	29%	11%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Training of Community champion planned in close coordination with NACO CSS team and SACS focal point person	Going on
2	The DISHA official were included in training cadre on CLM	Going on

GC7 Key Performance Indicator 4- Number of districts in which CLM has been rolled out

Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)				The CLM guidelines from NACO received in January 2026 to provide training to community champions and DISHA. The rolled out plan submitted – The plan is to integrate with SOCH, micro-plan for field roll out shared with NACO	
Denominator (Target)					
Achievement %					

S No.	Activities which were planned to be conducted with respect to this KPI	Status
	The CLM has not started by year -2	

GC7 Key Performance Indicator 5- Number of SLNs strengthened for Key Population

Key Performance Indicator	Y1 Achievement	Y2	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	0	3	3	In some states, the SACS and KP population took decision to strengthen and consider existing CBO as State level network - Maharashtra for FSW, MSM and TG - Gujarat SACS - considering existing MSM and TG CBOs	
Denominator (Target)	0	11	11		
Achievement %	0	27%	27%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	State Level Network Consultation with KP communities in 3 states (Gujarat, MP, Mizoram and UK) during April to June 2026 QTR	In the process
2	Discussion with SACS and KP networks is on going	In the process

GC7 Key Performance Indicator 1- Number of persons have been approached/reached on virtual platforms during the reporting period

Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	88800	126590	215390	N/A	NETREACH web portal
Denominator (Target)					
Achievement %					

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Innovative digital media campaign	Ongoing
2	Active online outreach in the dating apps and social media platforms	Ongoing

GC7 Key Performance Indicator 2- Number of person’s risk assessment have been completed during the reporting period

Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	5750	7983	13733	Proportion of individuals who completed risk assessment (target was at least 5%) among those who initiated risk assessment.	NETREACH web portal
Denominator (Target)	41585	36573	78158		Google Analytics
Achievement %	13.8%	21.8	17.6%		


S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Innovative digital media campaign	Ongoing
2	Active online outreach in the dating apps and social media platforms	Ongoing

GC7 Key Performance Indicator 3- Number of persons found at risk during the reporting period

Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	4062	8681	12743		NETREACH web portal
Denominator (Target)					
Achievement %					

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Innovative digital media campaign	Ongoing
2	Active online outreach in the dating apps and social media platforms	Ongoing


GC7 Key Performance Indicator 4- Number of persons tested for HIV during the reporting period



Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	2519	5917	8436	The program is dependant on self-reporting of PID for confirming HIV test; Several clients referred through NETREACH directly walk in to the ICTC and always do not report us with their PID number	NETREACH web portal
Denominator (Target)	4062	8681	12743		
Achievement %	62%	68%	66%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Innovative digital media campaign	Ongoing
2	Active online outreach in the dating apps and social media platforms	Ongoing

GC7 Key Performance Indicator 5- Percentage of HIV positive on ART during the reporting period



Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	190	563	753	Individuals who have shared their ART linked evidence are reported.	NETREACH web portal NETREACH web portal
Denominator (Target)	211	593	804		
Achievement %	90%	95%	94%		

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Innovative digital media campaign	Ongoing
2	Active online outreach in the dating apps and social media platforms	Ongoing

GC7 Key Performance Indicator 6- Number of persons tested for STI during the reporting period

Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	903	2879	3782		NETREACH web portal
Denominator (Target)					
Achievement %					

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Innovative digital media campaign	Ongoing
2	Active online outreach in the dating apps and social media platforms	Ongoing

GC7 Key Performance Indicator 7- WPTM activity: Demand generation through social media campaigns and awareness on virtual platforms. Mobilizing for self-assessment and referring for HIV-related services

Key Performance Indicator	Y1 Achievement	Y2 Achievement	Total Achievement	Reason for Variance	Source of Data
Numerator (KPI)	6.1 million	9.3 million	15.4 million		Meta and other advertising platforms
Denominator (Target)					
Achievement %					

S No.	Activities which were planned to be conducted with respect to this KPI	Status
1	Innovative digital media campaign	Ongoing
2	Active online outreach in the dating apps and social media platforms	Ongoing

Key Issues, Challenges in the last 2 years

S No.	Description	Timeline for Resolution/Overcoming
1	Complete address of LFU cases not available at ART	Captured alternative address from ICTC, white card and other sources Periodically addresses updated at the ARTCs by the CSC staff
2	TB notification among Prion inmates	Hand held Xray was introduced in Prison for identification of cases
3	Manipur internal situation	This is continuing to affect the essential outreach services and movement of PLHIV and ORW
4	Low salary of field worker with no increment, as a result attrition is high	Request to CCM and NACO to increased the salary of field team

Data Triangulation and Data Cleaning of ARTC

Objective

To identify duplicate beneficiaries who were reported as **Active on ART** at one ART Centre while simultaneously recorded as **LFU** at another ART Centre.

Implementation States

The exercise was initially launched in three states:

- Maharashtra
- Madhya Pradesh
- Gujarat

Process Followed

- ☐ A detailed proposal outlining the methodology and implementation process was submitted to NACO.
- ☐ The CST Division communicated the initiative to four SACS:
 1. Maharashtra
 2. Mumbai
 3. Gujarat
 4. Madhya Pradesh
- ☐ Active Data Managers from ART Centres were identified and oriented on the intervention.
- ☐ ART Centre line lists were compiled by Data Managers.
- ☐ Data were cross-matched within each state to identify potential duplicate cases.
- ☐ A total of **1371 duplicate cases** were identified among them MSACS-421 & MDACS 282 and remaining cases are from other states and reported to the respective SACS.
- ☐ Initial findings were presented to the CST Division and NACO.

Outcome

The exercise demonstrated significant value in improving data quality and beneficiary tracking. Based on the positive outcomes, NACO endorsed the approach and expanded the intervention to **13 high-burden states** for wider implementation and 5691 probable duplicate cases identified and SoP is developed for ARTC to address such cases



Activity and Timeline for the next 6 months

S No.	Activity	Timeline
1	Tracking of Lost to follow up cases	Sept-26
2	Strengthen Index testing - focus on vulnerable group who are at risk	
3	Proactive follow up of PPW and HEI in order to further move towards elimination of Vertical transmission	
4	HIV, STI and Viral hepatitis coverage for prison inmates	
5	Active case finding and TB notification among prison and other closed setting	
6	Reaching out to Hard to reach-Virtual population through virtual intervention and linking to Breakfree platform	

Thank You!

Founded in 1999, Alliance India is a non-governmental organisation operating in partnership with civil society, government and communities to support sustained responses to HIV in India that protect rights and improve health. Complementing the Indian national programme, we build capacity, provide technical support and advocate to strengthen the delivery of effective, innovative, community-based HIV programmes to vulnerable populations affected by the epidemic.

ALLIANCEINDIA.org

India HIV/AIDS Alliance
6 Community Centre, Zamrudpur
Kailash Colony Extension, New Delhi 110048
T +91-11-45367700

